

Project Name: **CENTERPOINT**

Formal TRC #6 Date: **11.07.2022**

Reviewer Name: **Mitesh Baxi**

Reviewer Department/Division: **PDT/Traffic Engineering**

---


- Please reconcile the street names and private/public ROWs on all the sheets. Plans still shows Street A/Street B labels on sheet like CR-103, CT-100.

**TECHNICAL STANDARDS:**

1. Remove City's 20'x70' sight distance triangle at the street intersection off Eastwood Rd and any other locations as applicable. 46'x46' is the relevant sight distance triangle.

**ROUNABOUT 1 (Swain Way/Center Point Dr):**

- Provide stopping sight distance on approach for an ADA ramp. Illustration in an image below.

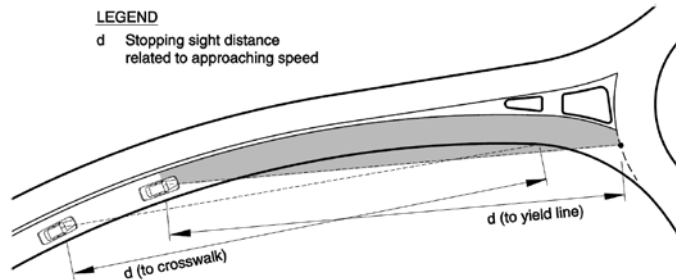

- Dimension the distance of crosswalk from entrance lines for all the legs. This distance should be approximately in increments of vehicle lengths.

**ROUNABOUT 2 (Calypso Dr/Cavalier Dr):**

- Auto-turns are shown on roundabout design without splitter island. Revise and show those on latest revision.

**SIGNAGE AND PAVEMENT MARKINGS:**

Please let me know if you have any questions or if I can be of further assistance.
